

Lab 2-Deliverables

Reflection Questions:

1. Did your estimations reflect the actual effort?

- Sprint 1 used the Fibonacci scale across multiple stories, totaling around 75 story points for the Lost/Found Reporting epics
- The remaining-values line showed a stepped decline rather than a smooth curve, meaning points were completed in batches rather than steadily
- Sprint 2 (25 points) showed an instant drop, with all work marked Done before the sprint's tracked timeline properly began
- Since both sprints were simulated quickly rather than run over real elapsed days, the estimates reflected anticipated complexity more than measured, day-by-day effort

2. Was your backlog well-prioritized?

- Yes. The backlog was structured into 5 clear epics, each broken into concrete user stories with priority levels
- Splitting work across two sprints by theme (Reporting-focused work in Sprint 1, Notifications/Claims work in Sprint 2) kept related functionality grouped
- High-priority items within each epic were addressed first, aligning with core user flows like reporting and claiming items

3. How did your simulated sprint align with your plan?


- Sprint 1 aligned well with the plan: story points declined steadily from ~75 to 0 across the sprint window
- Sprint 2 completed almost immediately at the start of its tracked window rather than gradually, since the underlying work was already done before the sprint dates were set
- The two sprints' assigned calendar dates overlapped rather than running sequentially in Jira, but the actual work execution was sequential — Sprint 1's stories were completed first, and Sprint 2's story was created and completed afterward
- This highlights a distinction between sprint metadata (the date range assigned to a sprint) and actual execution order (when work was really done) — a useful practical lesson, since real teams need both to align, not just one

4. What insights did the burndown chart give about your team's capacity?


- Sprint 1's step-pattern burndown suggests work was completed in clusters rather than at a steady daily pace, closer to how real teams often finish work near key checkpoints
- Sprint 2's near-instant drop suggests the sprint's formal tracking window didn't line up with when the actual work happened, a sign that sprint timing and real completion weren't fully synced in this simulation
- Comparing the two curves reinforced that a burndown chart is only a meaningful capacity signal when the sprint's dates genuinely bound when work occurs(a practical lesson about sprint tracking discipline as much as backlog planning)

Burndown Charts:

For Sprint1:

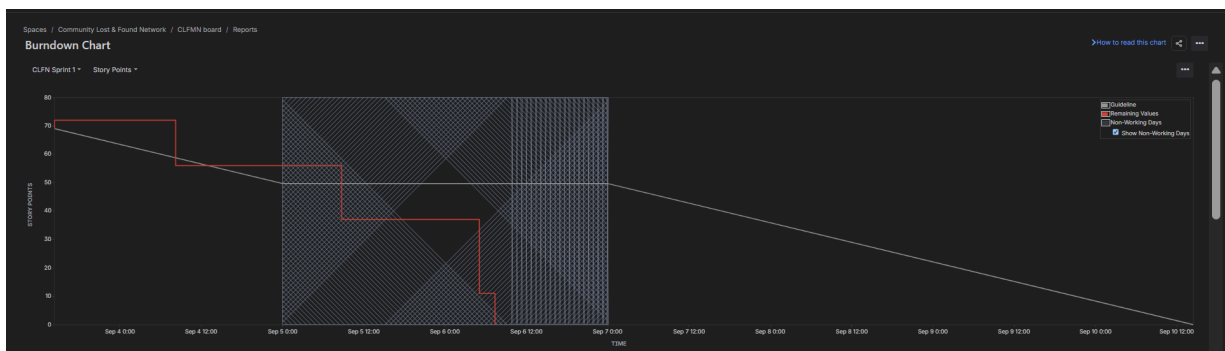

For Sprint2:

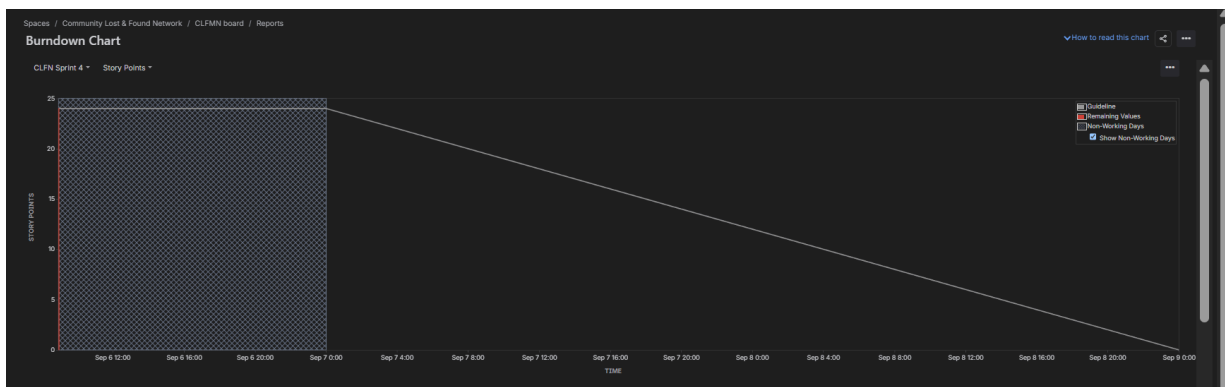

Epics:

Epic 1:

CLFN-1

1

Lost Item Reporting

To Do

</>

Improve Epic

+

Description

Enable owners to report lost items by providing a photo, text description, category, colour tag, last known location, and date lost, so that the system can use the information to identify potential matches with found items.

Child work items

100% Done

Work	Pri...	Stor...	As...	Status
☒ CLFN-6 Enter Lost Item Details	^ H.	5	U1	Done
☒ CLFN-8 Validate Required Information	^ H.	3	U1	Done
☒ CLFN-7 Submit Lost Item Report	^ H.	3	U1	Done

Linked work items

Add linked work item

Confluence content

Project plan

Try template

Details

Assignee

Unassigned
Assign to me

Reporter

Navya S

Epic 2:

CLFN-2

1

Found Item Reporting

To Do ▾

</>

⚡

➕ Improve Epic

...

+

Description

Enable finders to submit found item posts with a photo, text description, category, colour tag, and current geographical location, so that the system can identify and match the found item with lost item reports.

Child work items

...

+

100% Done

Work	Pri...	Stor...	As...	Status
☒ CLFN-11 Capture Found Item Location	^ H.	3	U	Done ▾
☒ CLFN-9 Enter Found Item Details	^ H.	5	U	Done ▾
☒ CLFN-10 Submit Found Item Report	^ H.	3	U	Done ▾

Linked work items

Add linked work item

Epic 3:

CLFN-3

1

Lost & Found Matching

To Do

Improve Epic

Description

Enable the system to automatically match newly logged found items with active lost item reports using category, colour tag, and location radius, and provide a match probability to identify potential matches.

Child work items

100% Done

Work	Pri...	Stor...	As...	Status
☒ CLFN-12 Match Found Items with Lost Reports	H.	8	Ui	Done
☒ CLFN-14 Perform Fast Location-Based Matching	M.	8	Ui	Done
☒ CLFN-13 Calculate Match Probability	H.	5	Ui	Done

Linked work items

Add linked work item

Confluence content

Project plan

Try template

Details

Assignee

Unassigned

Assign to me

Reporter

NS Navya S

Epic 4:

CLFN-4

1

Claim & Ownership Verification

To Do

Improve Epic

Description

Enable owners to securely claim found items by answering private security questions set by the finder before contact details are revealed, ensuring that only legitimate claimants can verify ownership.

Child work items

100% Done

Work	Pri...	Stor...	As...	Status
☒ CLFN-17 Exchange Contact Details After Verification	H.	5	Ui	Done
☒ CLFN-15 Claim Found Item	H.	5	Ui	Done
☒ CLFN-16 Verify Ownership with Security Questions	H.	8	Ui	Done
☒ CLFN-21 Mark Claim as Verified	M.	2	Ui	Done

Linked work items

Add linked work item

Confluence content

Project plan

Try template

Details

Assignee

Unassigned

Assign to me

Reporter

Naura S

Epic 5:

CLFN-5

1



Notifications & Community Moderation

To Do ▾



⚡ Improve Epic



Description

Enable the system to notify owners about candidate matches and allow community administrators to flag suspicious matches and remove associated lost or found posts from active listings.

Child work items

... ▢ +

100% Done

Work	Pri...	Stor...	As...	Status
☒ CLFN-20 Remove Suspicious Listings	= M.	5	U1	Done ▾
☒ CLFN-19 Flag Suspicious Match	= M.	3	U1	Done ▾
☒ CLFN-18 Notify Owner of Candidate Match	= M.	3	U1	Done ▾

Linked work items

Add linked work item

Confluence content ⓘ

...

☒ Project plan

Try template

Details

Assignee


Unassigned

[Assign to me](#)

Reporter

Navya S

Active Sprints Board:

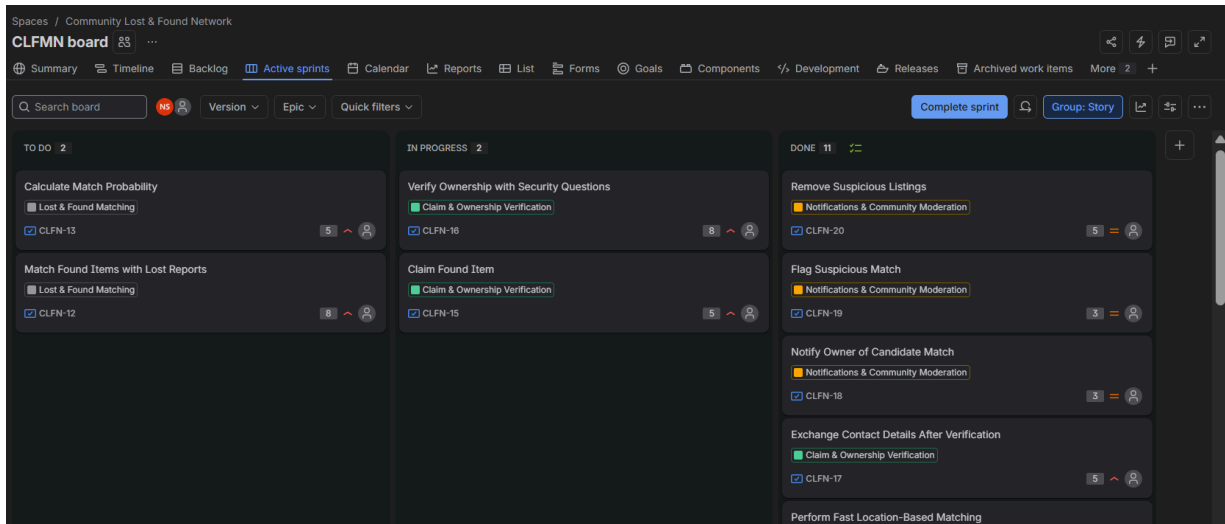

Dashboard View:

